


Rocky Mountain Power
Exhibit RMP___(TJH-2SD)
Docket No. 20000-519-EA-17
Witness: Timothy J. Hemstreet

BEFORE THE WYOMING PUBLIC SERVICE
COMMISSION

ROCKY MOUNTAIN POWER

Exhibit Accompanying Supplemental Direct Testimony of Timothy J. Hemstreet
Repowering Project – Schedule

February 2018

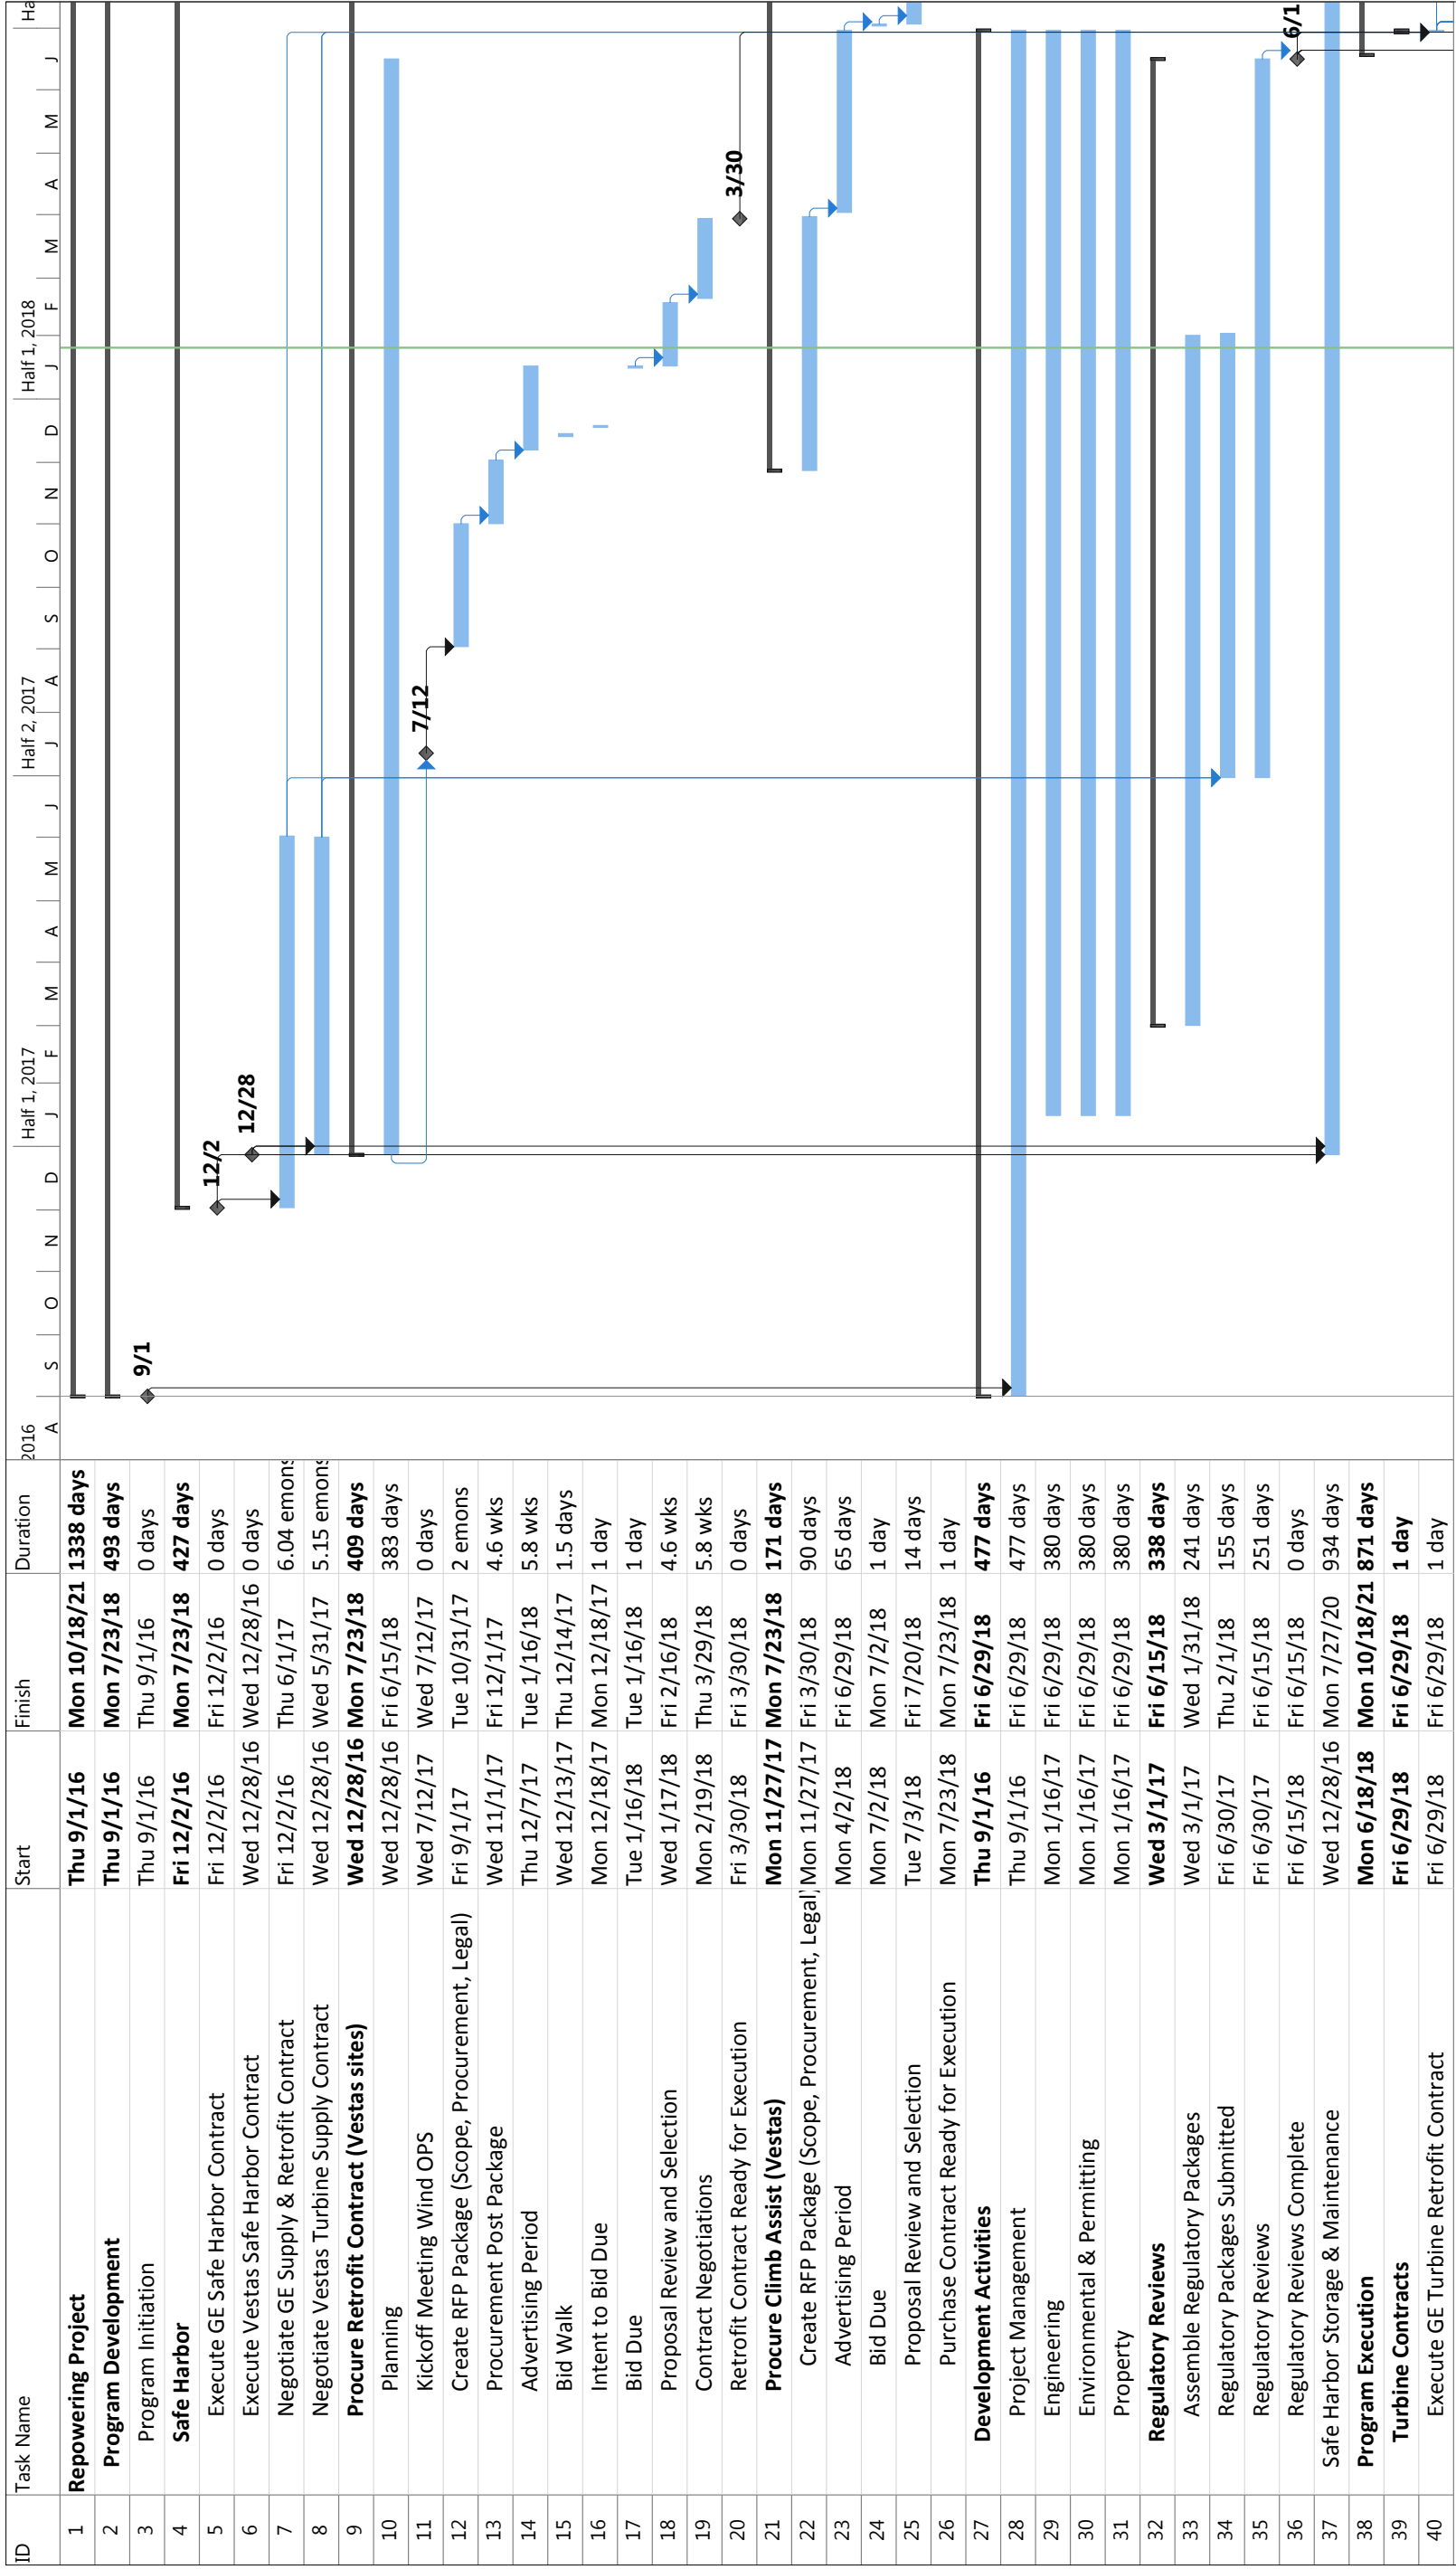


ID	Task Name	Start	Finish	Duration	2016	A	S	O	N	D	Half 1, 2017	J	F	M	A	M	A	Half 1, 2018	J	D	Ha
83	Issue WTG Supply and Retrofit Contract Release	Fri 6/29/18	Fri 6/29/18	0 days																	
84	WTG Fabrication	Fri 6/29/18	Sun 2/24/19	8 emons																	
85	Site Civil Works / BOP	Mon 7/2/18	Mon 7/1/19	261 days																	
86	Transport and Delivery	Mon 2/25/19	Fri 6/7/19	15 wks																	
87	WTG Installation	Mon 3/18/19	Fri 6/28/19	15 wks																	
88	Substantial Completion	Mon 7/1/19	Mon 7/1/19	0 days																	
89	Final Completion	Fri 7/19/19	Fri 7/19/19	0 days																	
90	Project Closeout	Fri 7/19/19	Wed 1/15/20	6 emons																	
91	Seven Mile Hill II	Fri 6/29/18	Wed 1/15/20	403 days																	
92	Issue WTG Supply and Retrofit Contract Release	Fri 6/29/18	Fri 6/29/18	0 days																	
93	WTG Fabrication	Fri 6/29/18	Sun 2/24/19	8 emons																	
94	Site Civil Works / BOP	Mon 7/2/18	Mon 7/1/19	261 days																	
95	Transport and Delivery	Mon 2/25/19	Fri 6/7/19	15 wks																	
96	WTG Installation	Mon 3/18/19	Fri 6/28/19	15 wks																	
97	Substantial Completion	Mon 7/1/19	Mon 7/1/19	0 days																	
98	Final Completion	Fri 7/19/19	Fri 7/19/19	0 days																	
99	Project Closeout	Fri 7/19/19	Wed 1/15/20	6 emons																	
100	High Plains/McFadden Ridge Area	Mon 10/22/18	Sun 5/17/20	410 days																	
101	High Plains	Mon 10/22/18	Sun 5/17/20	410 days																	
102	Issue WTG Supply and Retrofit Contract Release	Mon 10/22/18	Mon 10/22/18	0 days																	
103	WTG Fabrication	Mon 10/22/18	Wed 6/19/19	8 emons																	
104	Site Civil Works / BOP	Mon 10/22/18	Tue 10/29/19	267 days																	
105	Transport and Delivery	Wed 6/19/19	Tue 10/8/19	16 wks																	
106	WTG Installation	Wed 6/19/19	Tue 10/29/19	19 wks																	
107	Substantial Completion	Tue 10/29/19	Tue 10/29/19	0 days																	
108	Final Completion	Tue 11/19/19	Tue 11/19/19	0 days																	
109	Project Closeout	Tue 11/19/19	Sun 5/17/20	6 emons																	
110	McFadden Ridge	Mon 10/22/18	Sun 5/17/20	410 days																	
111	Issue WTG Supply and Retrofit Contract Release	Mon 10/22/18	Mon 10/22/18	0 days																	
112	WTG Fabrication	Mon 10/22/18	Wed 6/19/19	8 emons																	
113	Site Civil Works / BOP	Mon 10/22/18	Tue 10/29/19	267 days																	
114	Transport and Delivery	Wed 6/19/19	Tue 10/8/19	16 wks																	
115	WTG Installation	Wed 6/19/19	Tue 10/29/19	19 wks																	
116	Substantial Completion	Tue 10/29/19	Tue 10/29/19	0 days																	
117	Final Completion	Tue 11/19/19	Tue 11/19/19	0 days																	
118	Project Closeout	Tue 11/19/19	Sun 5/17/20	6 emons																	
119	Dunlap	Wed 12/18/19	Mon 5/31/21	379 days																	
120	Issue WTG Supply and Retrofit Contract Release(s)	Wed 12/18/19	Wed 12/18/19	0 days																	
121	WTG Fabrication	Wed 12/18/19	Thu 7/30/20	7.5 emons																	
122	Site Civil Works / BOP	Wed 12/18/19	Wed 11/11/20	236 days																	


Project: Repower Schedule
 Date: Fri 1/26/18

Task Split Milestone


Summary Project Summary

Page 3

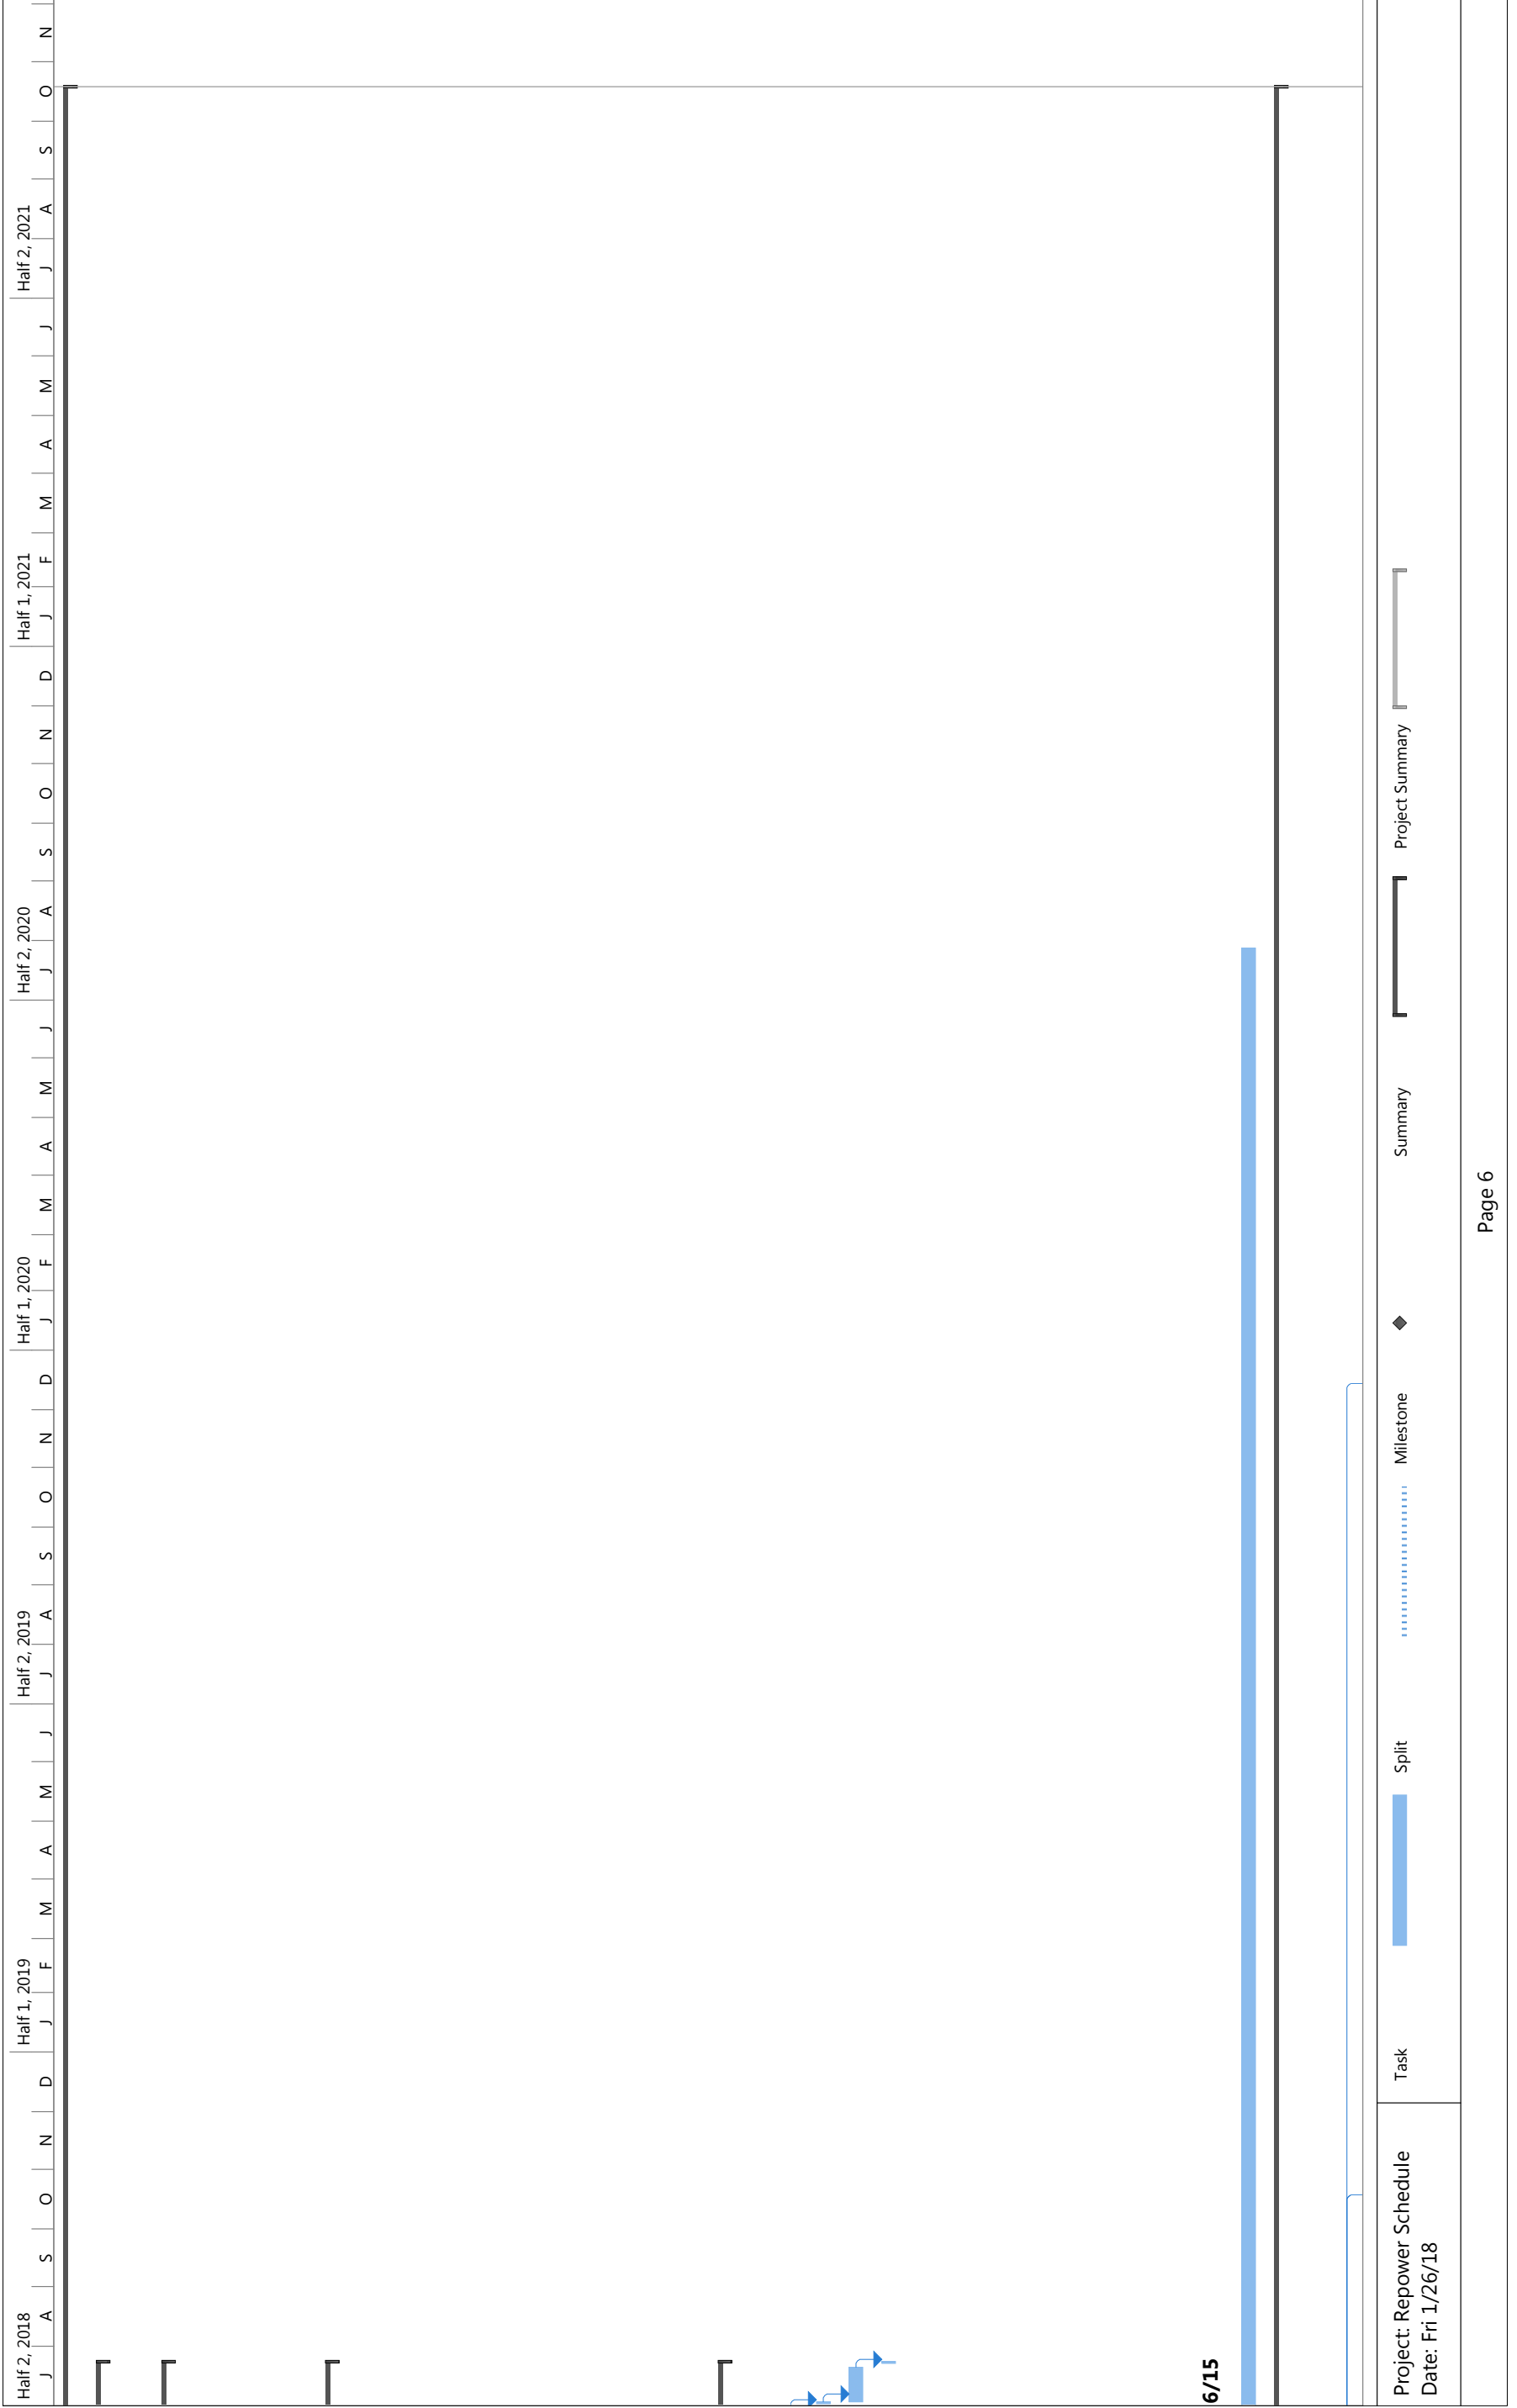


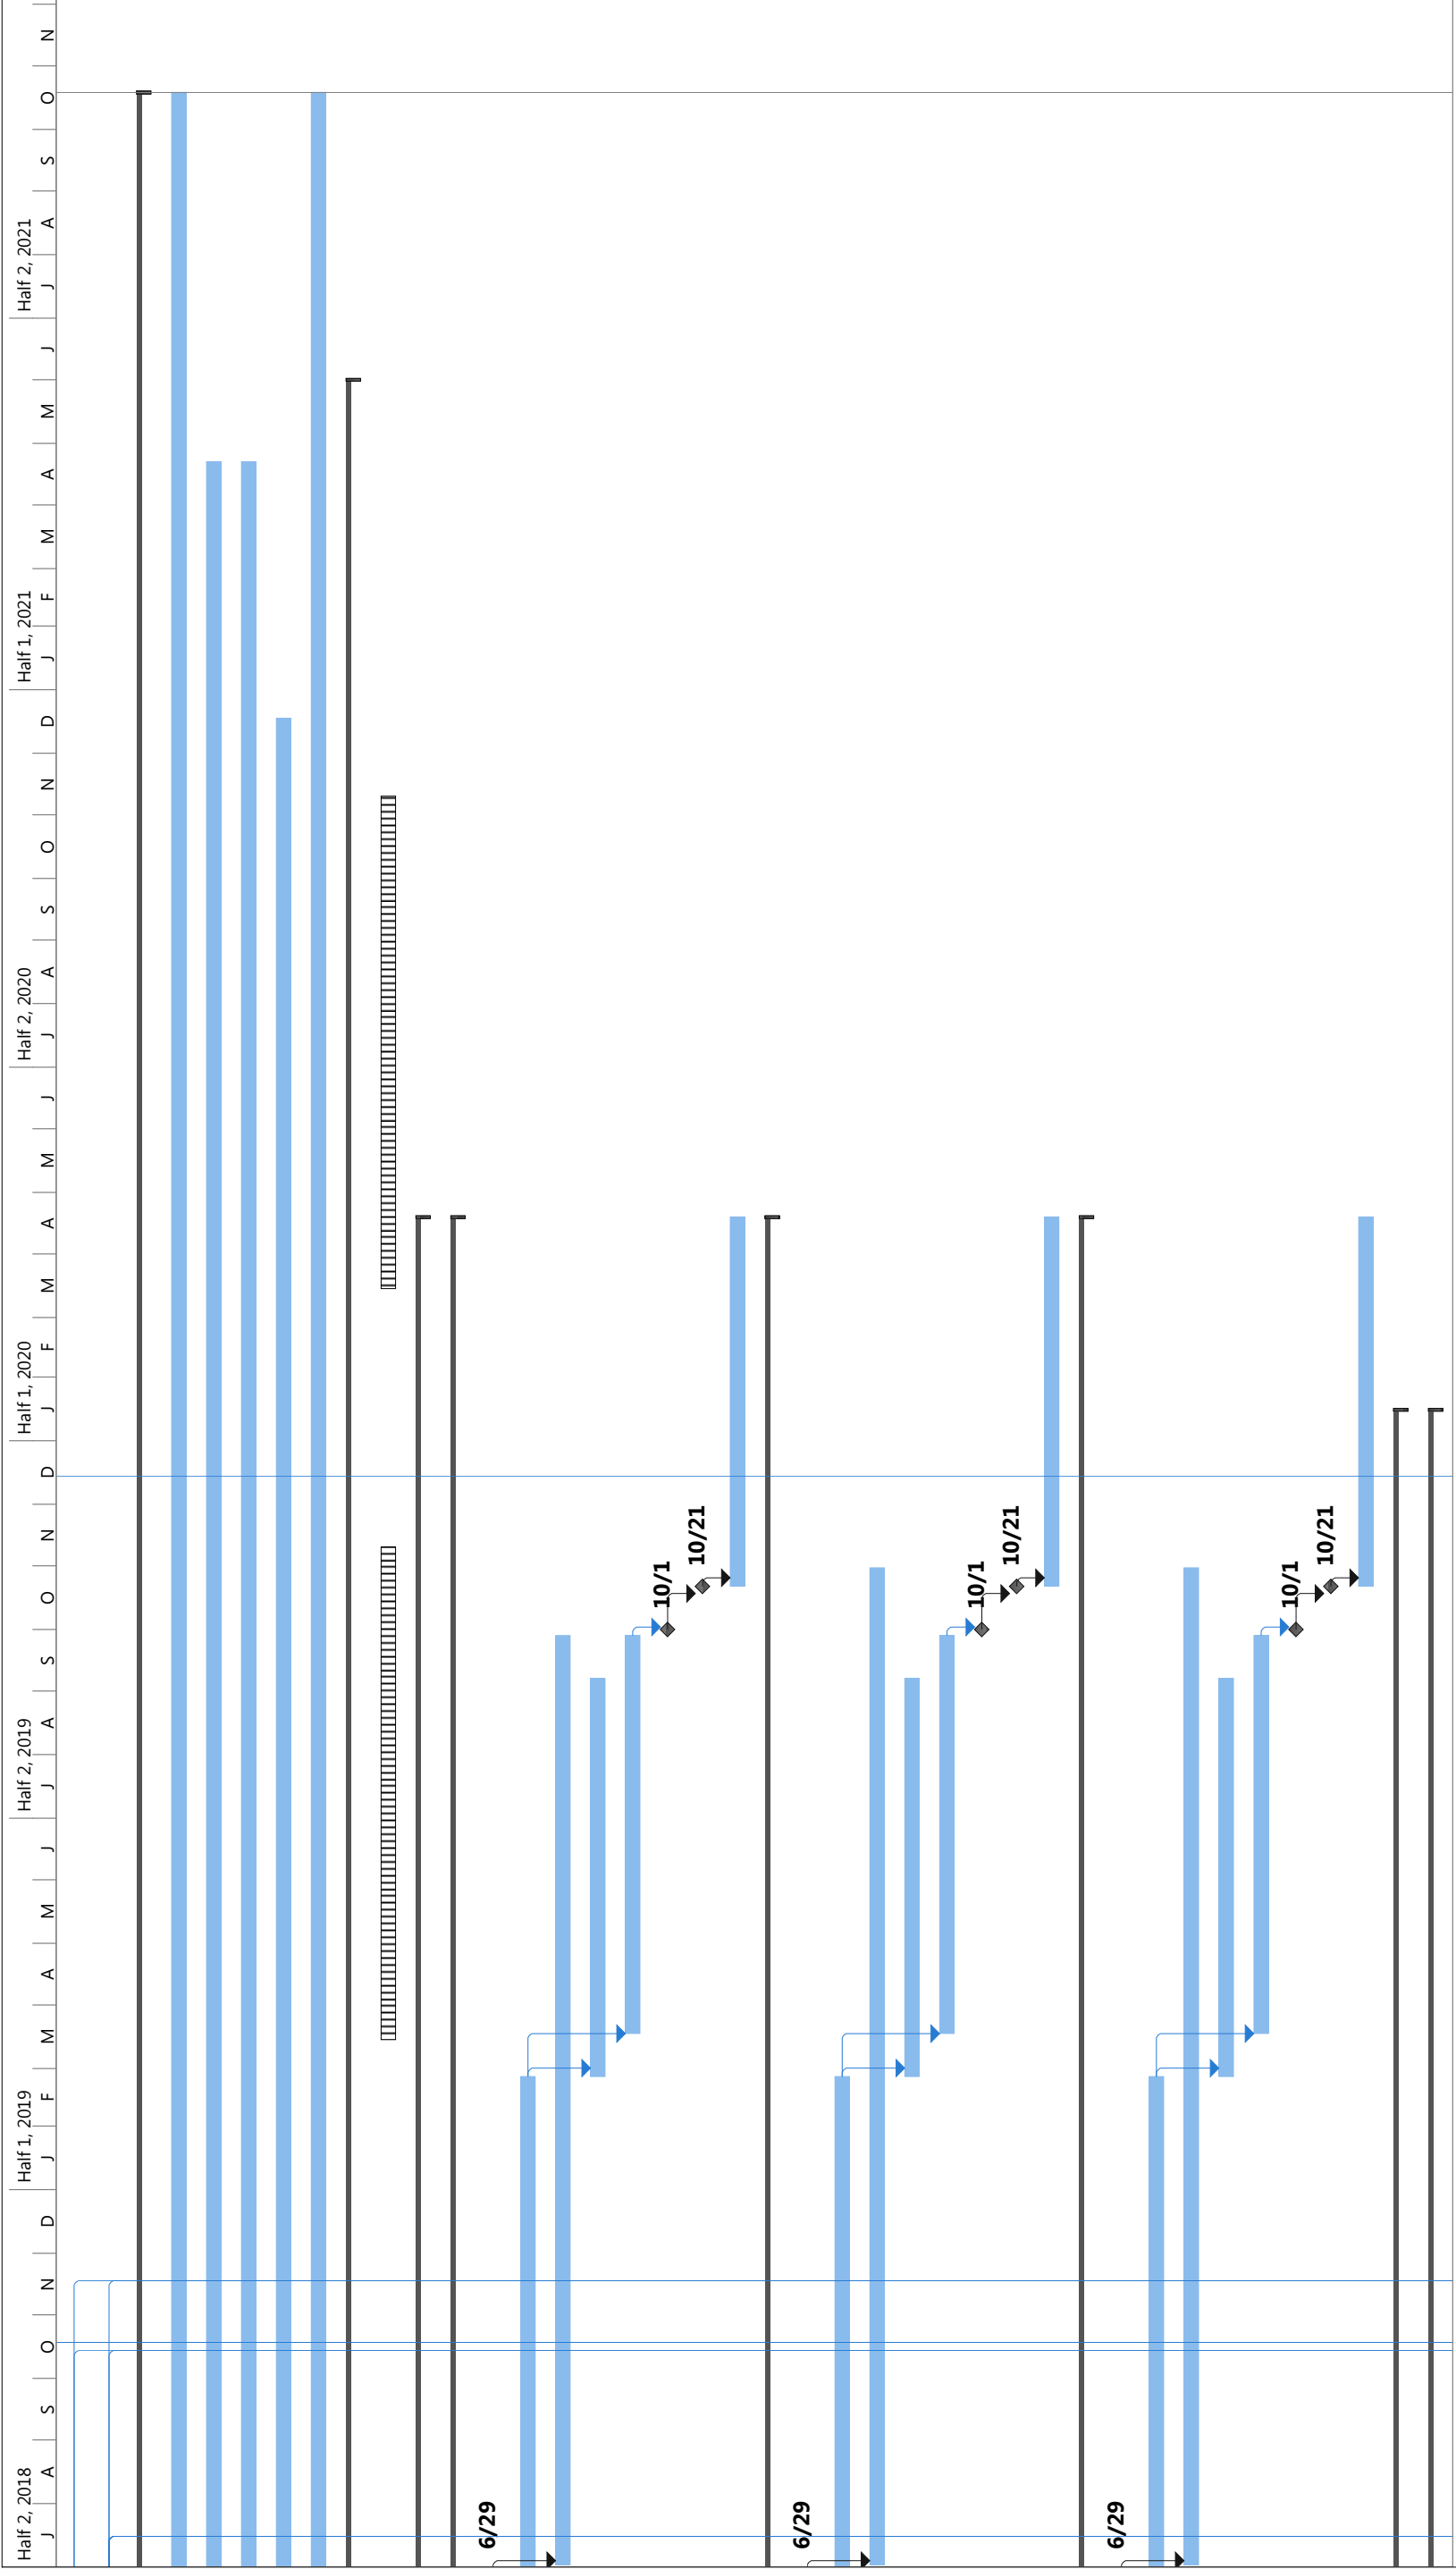

Project: Repower Schedule Date: Fri 1/26/18		Task	Split	Milestone	Summary	Project Summary
--	--	------	-------	-----------	---------	-----------------

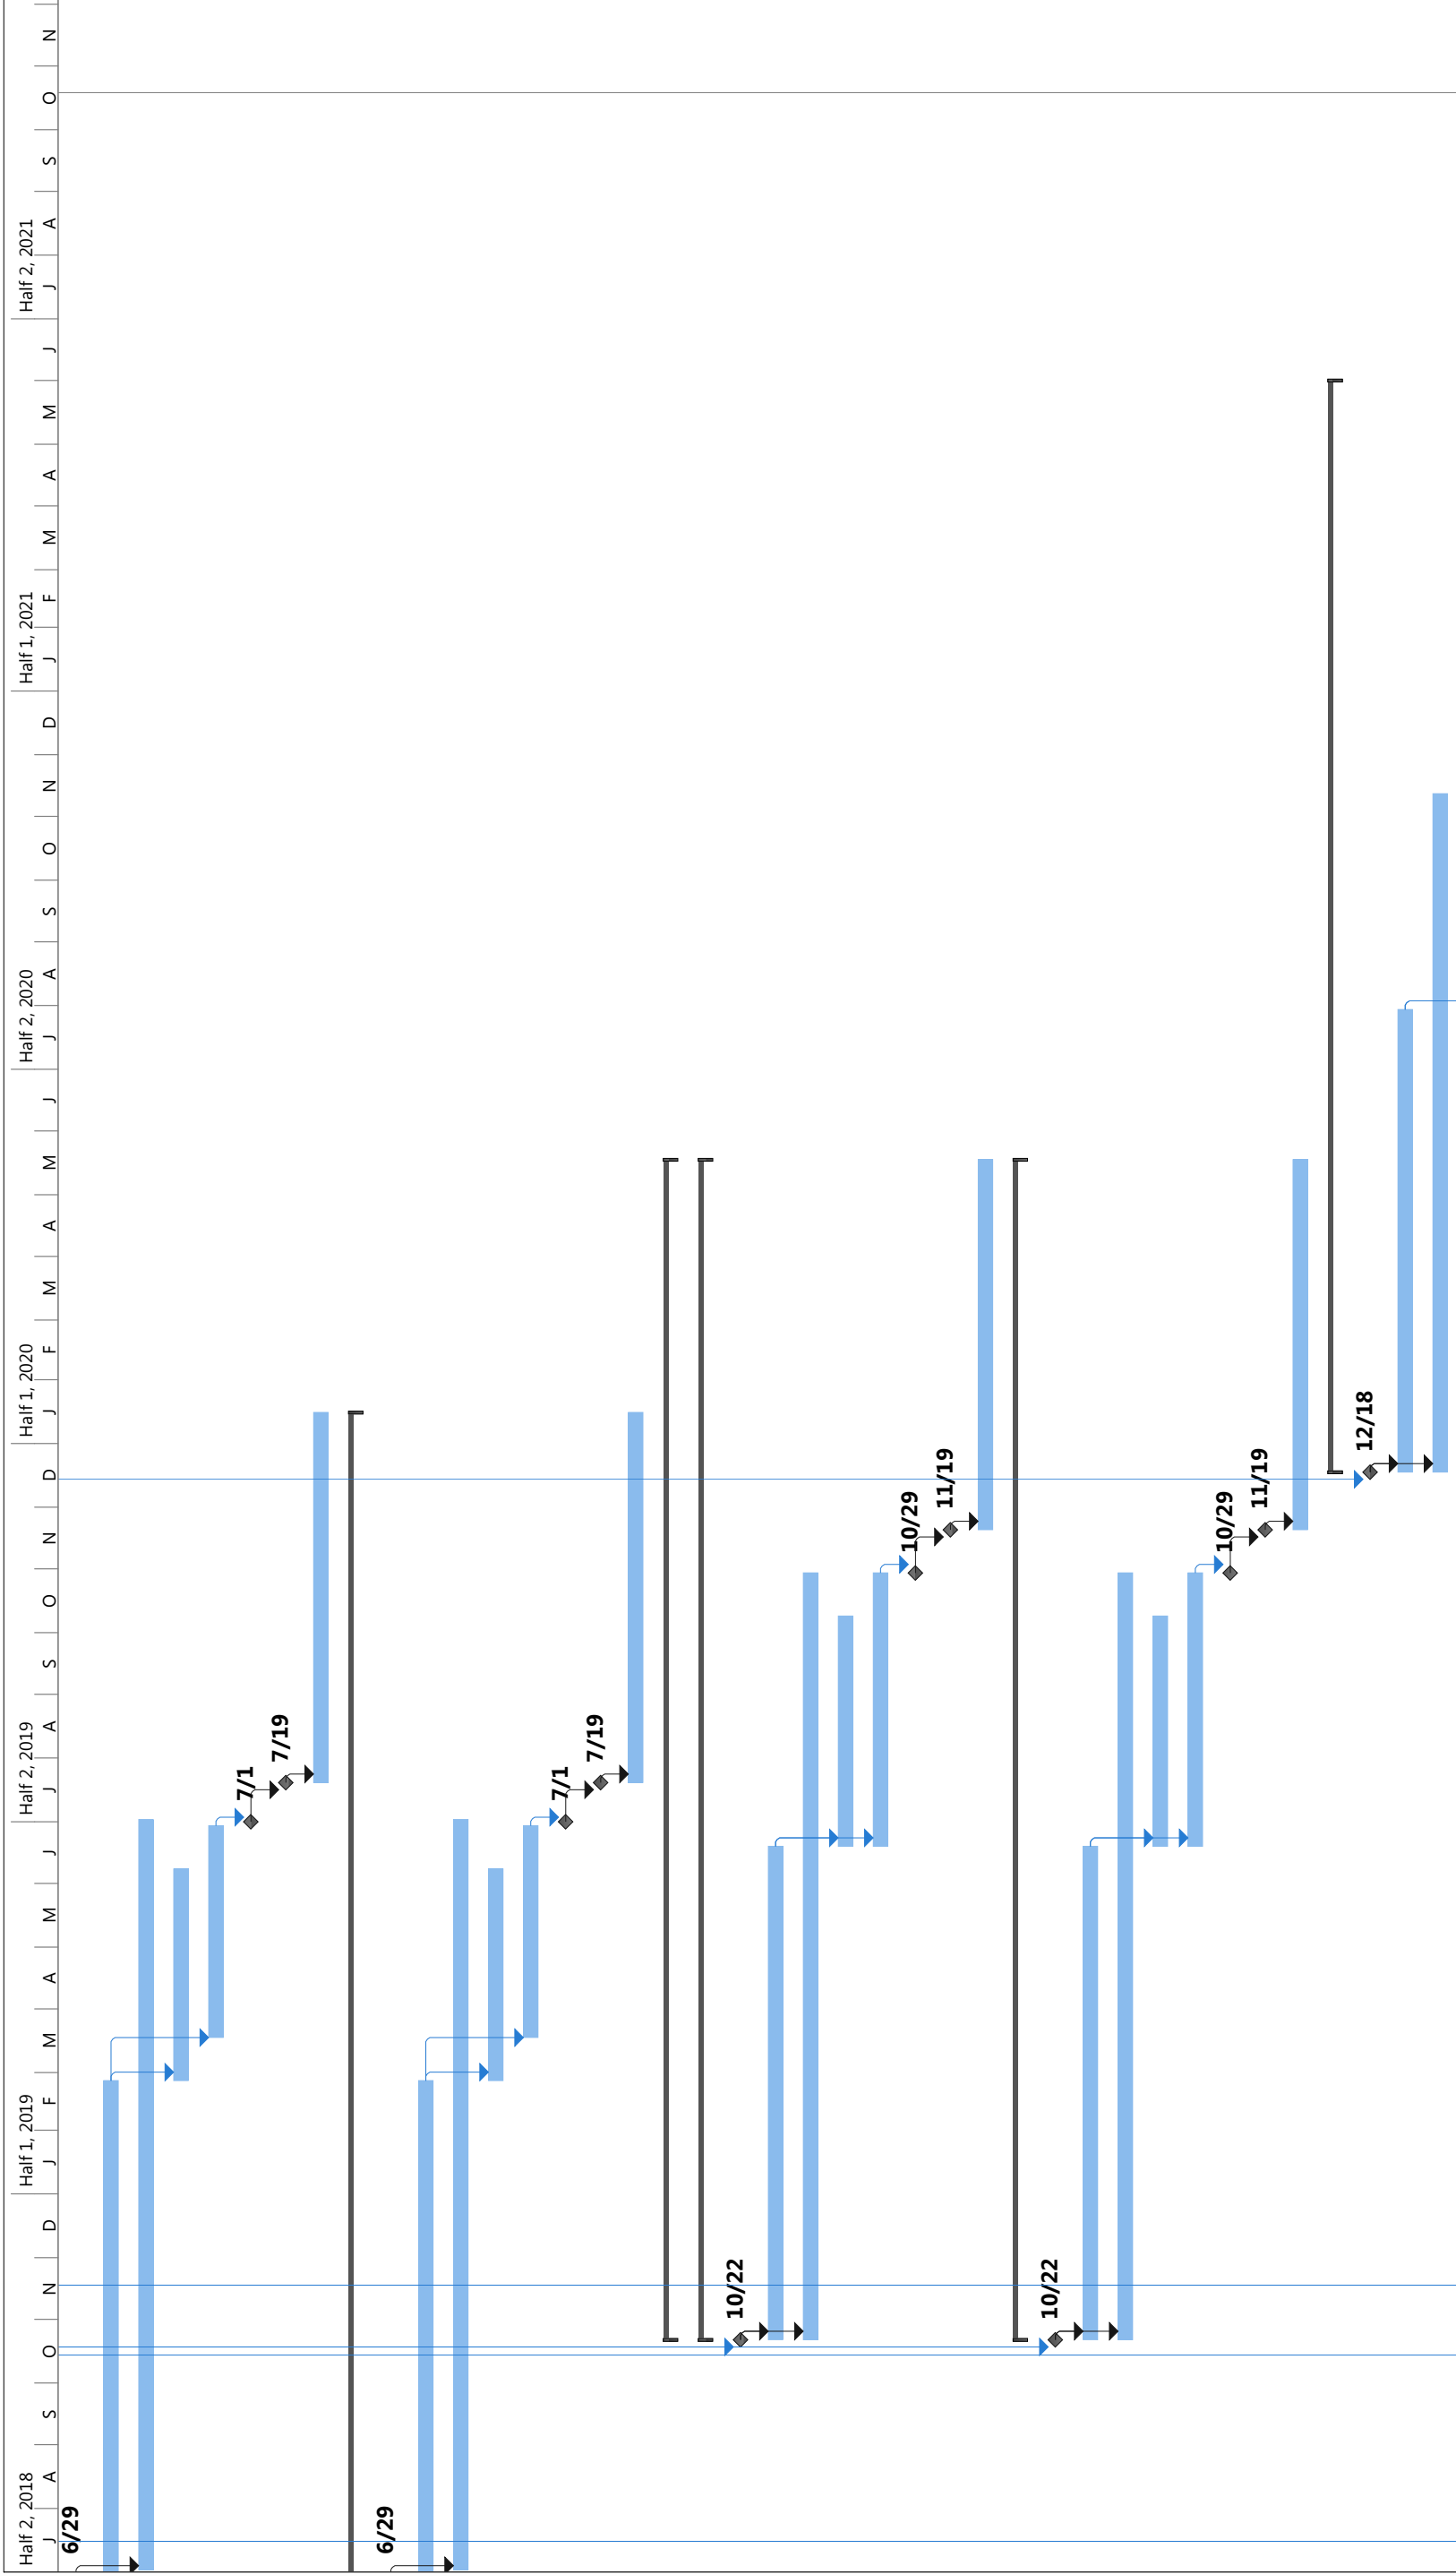

Project: Repower Schedule Date: Fri 1/26/18		Task	Split	Milestone	Summary	Project Summary
--	--	------	-------	-----------	---------	-----------------

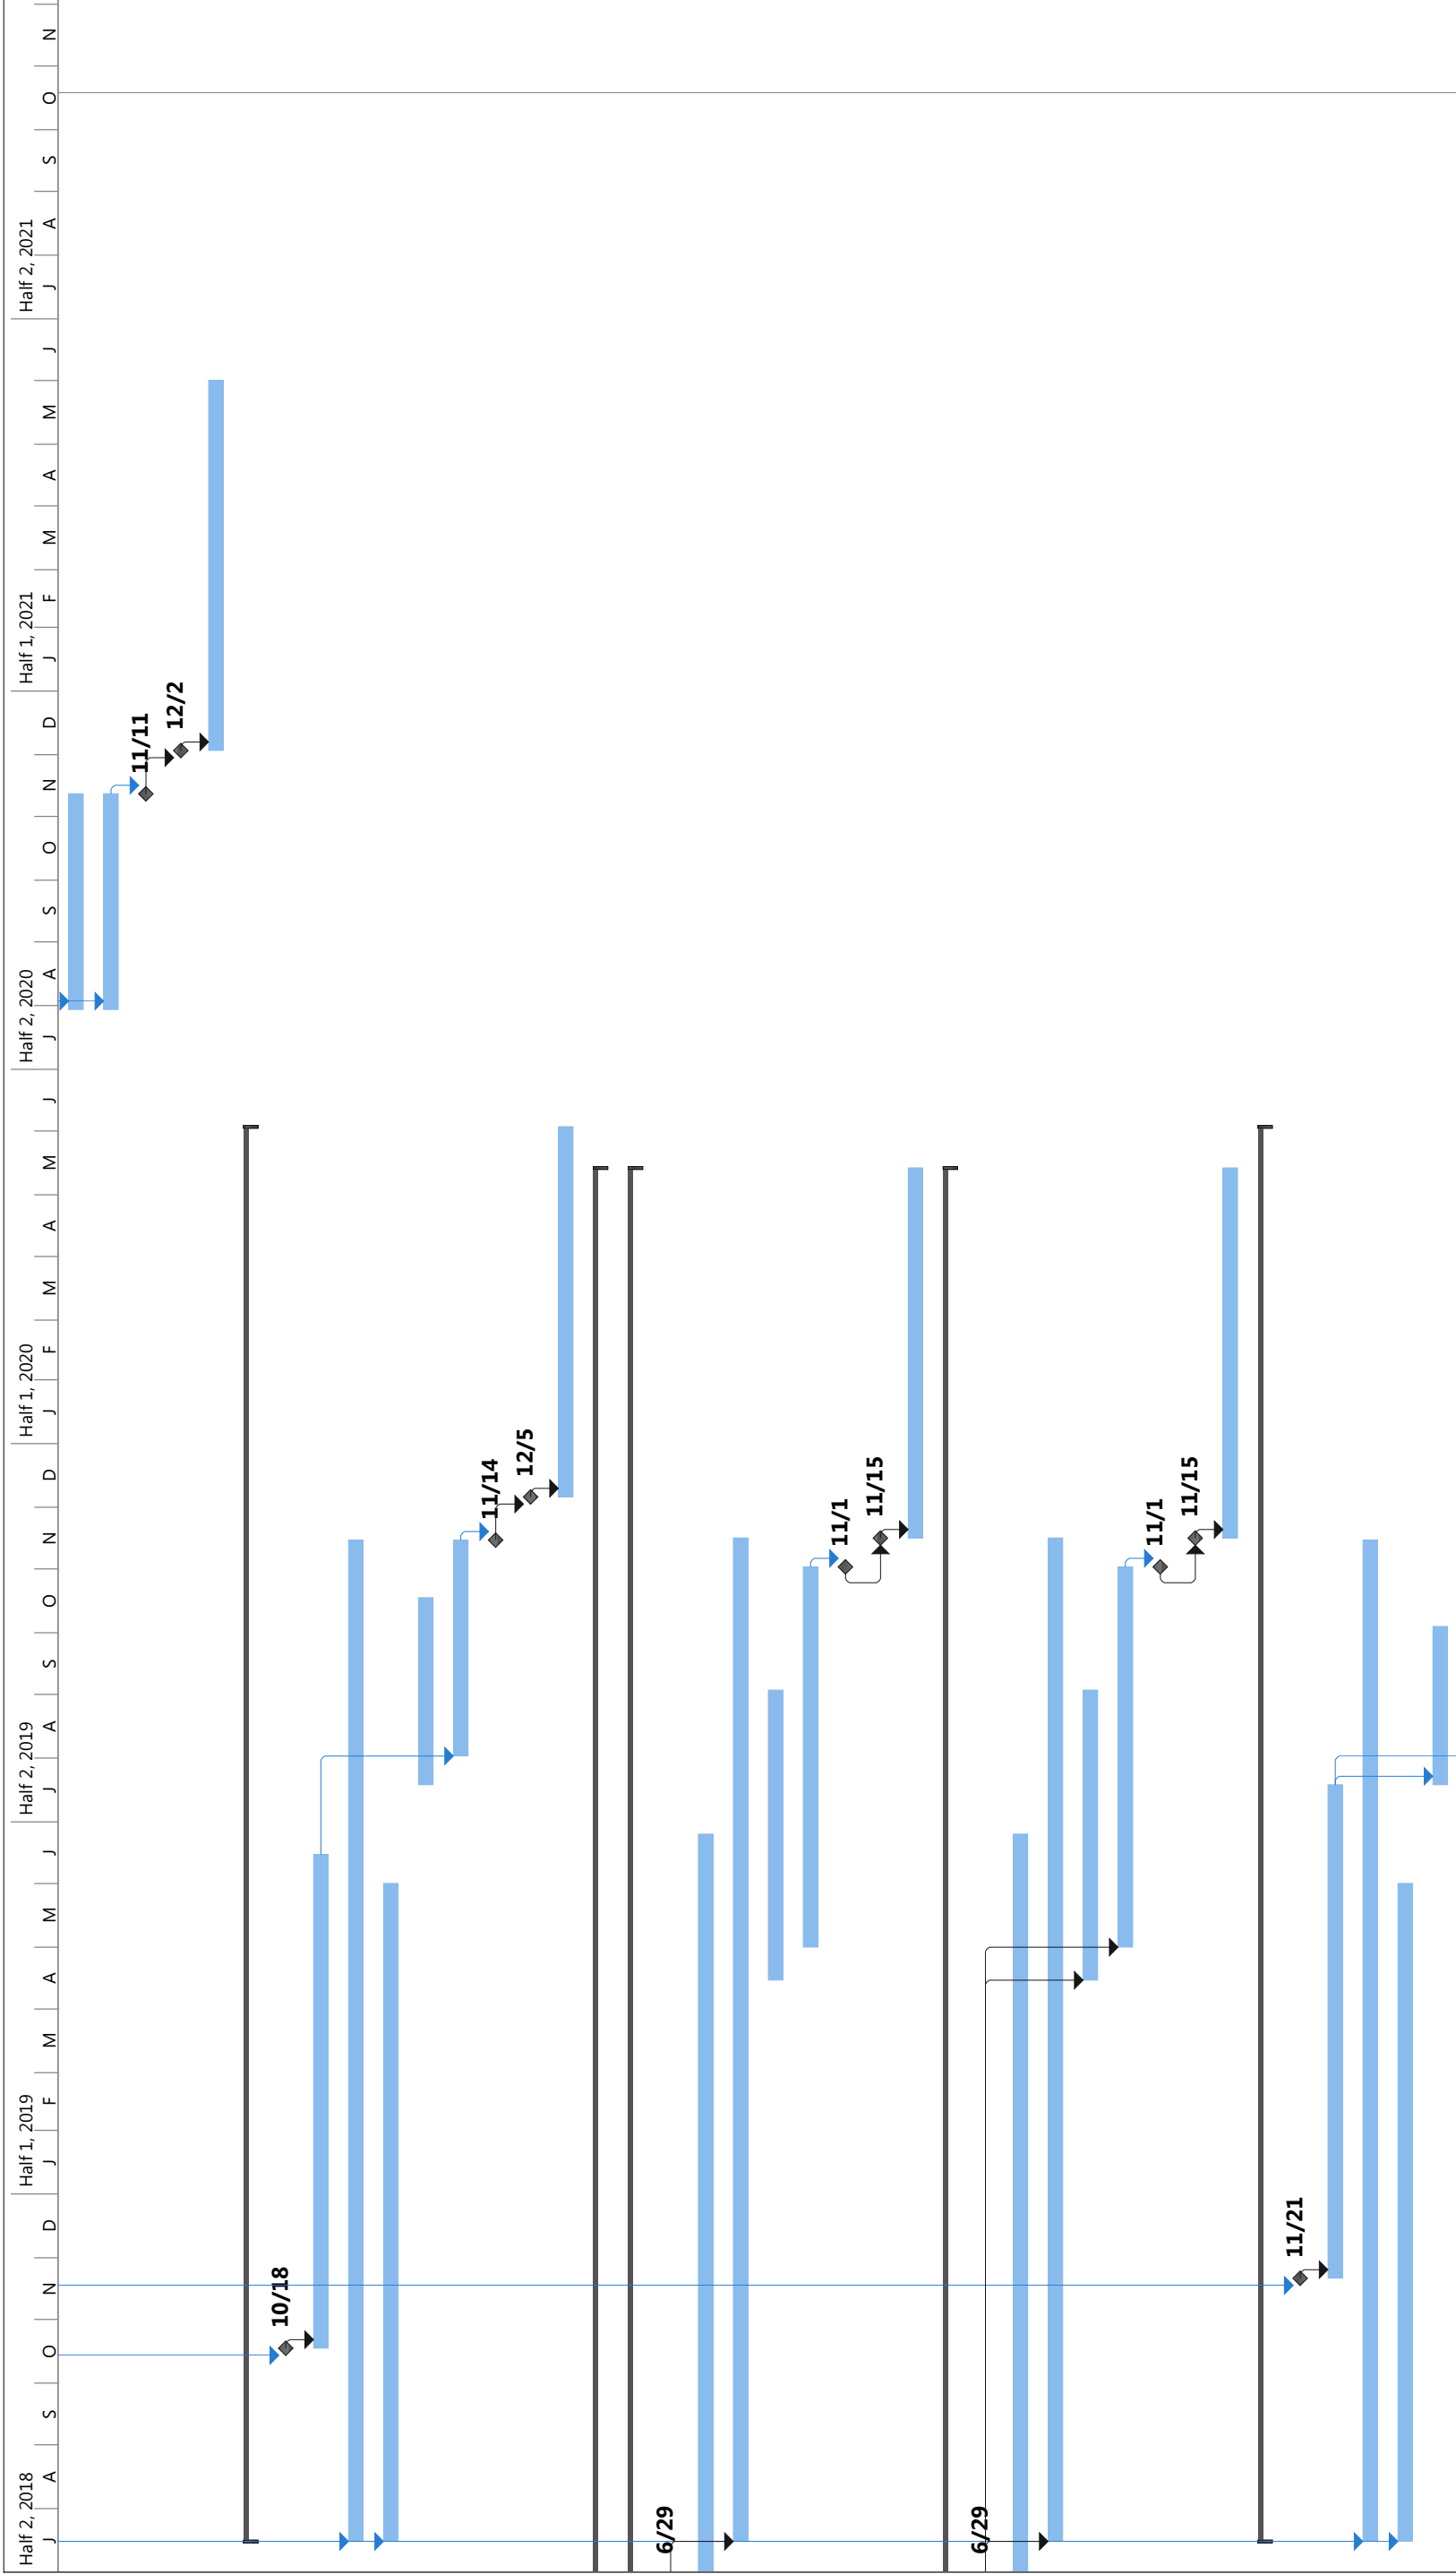

Project: Repower Schedule
 Date: Fri 1/26/18

Task
 Split
 Milestone
 Summary
 Project Summary

